



**BOSTON WATER & SEWER COMMISSION**  
**SOUTH BOSTON SEWER SEPARATION PROJECT**  
**Contract No. 20-309-012**  
**Report for January 1 through January 31, 2023**

## OVERALL PROJECT UPDATE

The Boston Water and Sewer Commission's (the Commission) South Boston Sewer Separation Project involves separating the combined sewer system in South Boston. The purpose of this project is to reduce pollution levels in Boston Harbor by substantially decreasing the number and volume of Combined Sewer Overflows (CSOs) into Fort Point Channel and Boston Harbor. The separation project is being undertaken by the Commission in association with the Massachusetts Water Resources Authority (MWRA).

The South Boston Sewer Separation Project encompasses an area roughly delineated by Interstate 93 to the west, West Broadway, and West Second Street to the north and east, G Street to the east, and Devine Way to the south. Land use in the project area is characterized by residential neighborhoods; light industrial and large commercial buildings and complexes; small business and retail districts; civic, cultural, and educational facilities; and transportation-related sites.

## CONTRACT 1 UPDATE – THROUGH JANUARY 31, 2022

Over the month of January, the project contractor completed sewer installation on Flaherty Way from B Street to St. Casmir Street and completed sewer installation on St. Casmir Street from Flaherty Way to Crowley Rogers Way.

## ONGOING AND UPCOMING WORK

Currently, the contractor plans on continuing work with one crew within BHA property with a focus on sewer and drain installation on Flaherty Way from B Street towards D Street.



*24" sewer installation on Flaherty Way.*

# INSTALLATION OF NEW STORM DRAINS, SANITARY SEWERS AND WATER MAINS IN SOUTH BOSTON – CONTRACT 1



Contractor: Fed. Corp., Dedham, Massachusetts  
Status as of January 31, 2022

Contract No. 20-309-012

## MAJOR PROGRESS ITEMS – LINEAR FEET (LF) AND % INSTALLED TO DATE

12" – 48" Drain	3,807 LF	67.98%
10" – 24" Sewer	6,762 LF	76.75%
4" – 20" Water Main	5,050 LF	68.19%

## SCHEDULING SUMMARY

Notice to Proceed:	07/06/2021
Work Commenced:	08/10/2021
Anticipated Completion Date:	05/26/2023

## SCHEDULE ASSESSMENT

The contractor has completed 319 of 400 working days with 79.8% of time used and 20.2% of time remaining.

## PUBLIC AFFAIRS: COMPLAINTS RECEIVED VIA EMAIL AND PHONE (PROJECT TOTAL)

Parking/access	3
Loss/discoloration of water, or low pressure	3
Sewer break/back up	0
Noise/dust/debris	0
Damage	2
Other	7


**Project Total** **15**

## PUBLIC AFFAIRS: CALLS REGARDING OTHER UTILITIES' WORK OR FACILITIES' ACTIVITIES

Parking/access and other issues	0
<b>Other Total</b>	<b>0</b>

## SAFETY

Incidents reported this period	0
<b>Incidents reported to-date</b>	<b>0</b>

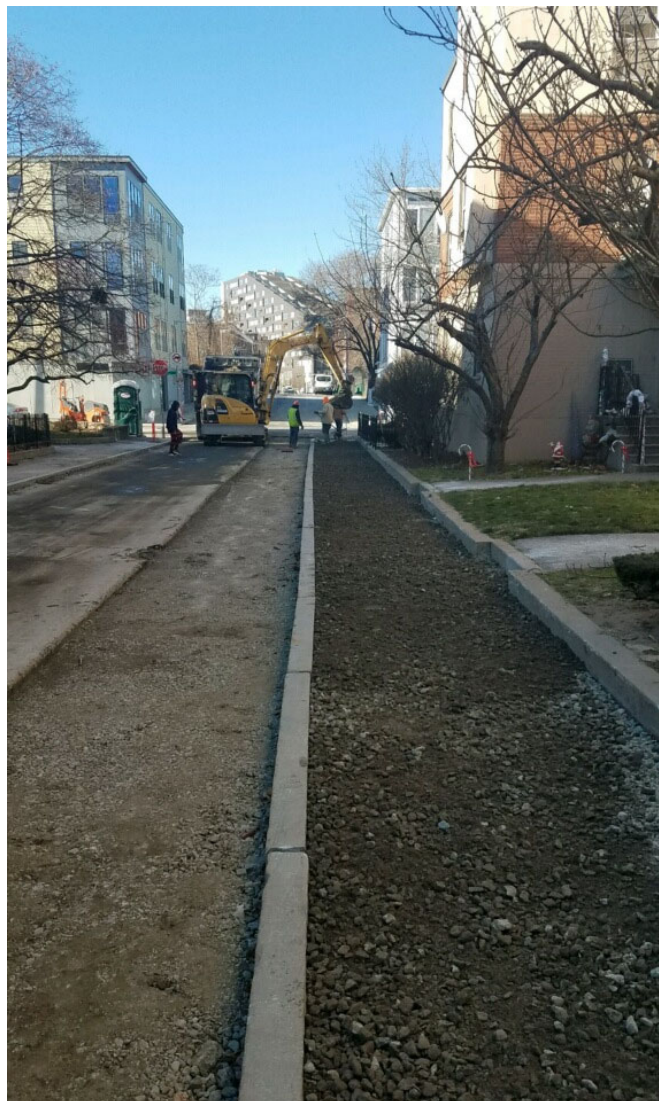

*Roadway preparation on Crowley Rogers Way.*

Contact us at:

Project Field Office Voicemail: 617-865-9299 (daytime) or 617-989-7900 (24/7 emergency)

Email: [sbss@bwsc.org](mailto:sbss@bwsc.org)
