



**BOSTON WATER & SEWER COMMISSION**  
**SOUTH BOSTON SEWER SEPARATION PROJECT**  
**Contract No. 20-309-012**  
*Report for April 1 through April 30, 2023*

## OVERALL PROJECT UPDATE

The Boston Water and Sewer Commission's (the Commission) South Boston Sewer Separation Project involves separating the combined sewer system in South Boston. The purpose of this project is to reduce pollution levels in Boston Harbor by substantially decreasing the number and volume of Combined Sewer Overflows (CSOs) into Fort Point Channel and Boston Harbor. The separation project is being undertaken by the Commission in association with the Massachusetts Water Resources Authority (MWRA).


The South Boston Sewer Separation Project encompasses an area roughly delineated by Interstate 93 to the west, West Broadway, and West Second Street to the north and east, G Street to the east, and Devine Way to the south. Land use in the project area is characterized by residential neighborhoods; light industrial and large commercial buildings and complexes; small business and retail districts; civic, cultural, and educational facilities; and transportation-related sites.

## CONTRACT 1 UPDATE – THROUGH APRIL 30, 2023

Over the month of April, the project contractor completed work on Flaherty Way from B Street to D Street resetting curb, placing sidewalks and temporary paving; installed sewer, placed sidewalks and temporary paving on Orton Marotta Way; and completed drain installation on Joyce Hayes Way and placed temporary paving.

## ONGOING AND UPCOMING WORK

Currently, the contractor plans on installing water on West Fourth Street across B Street into Crowley Rogers Way and continue with water and sewer on Crowley Rogers Way, and restart water and sewer installation on West Seventh Street.

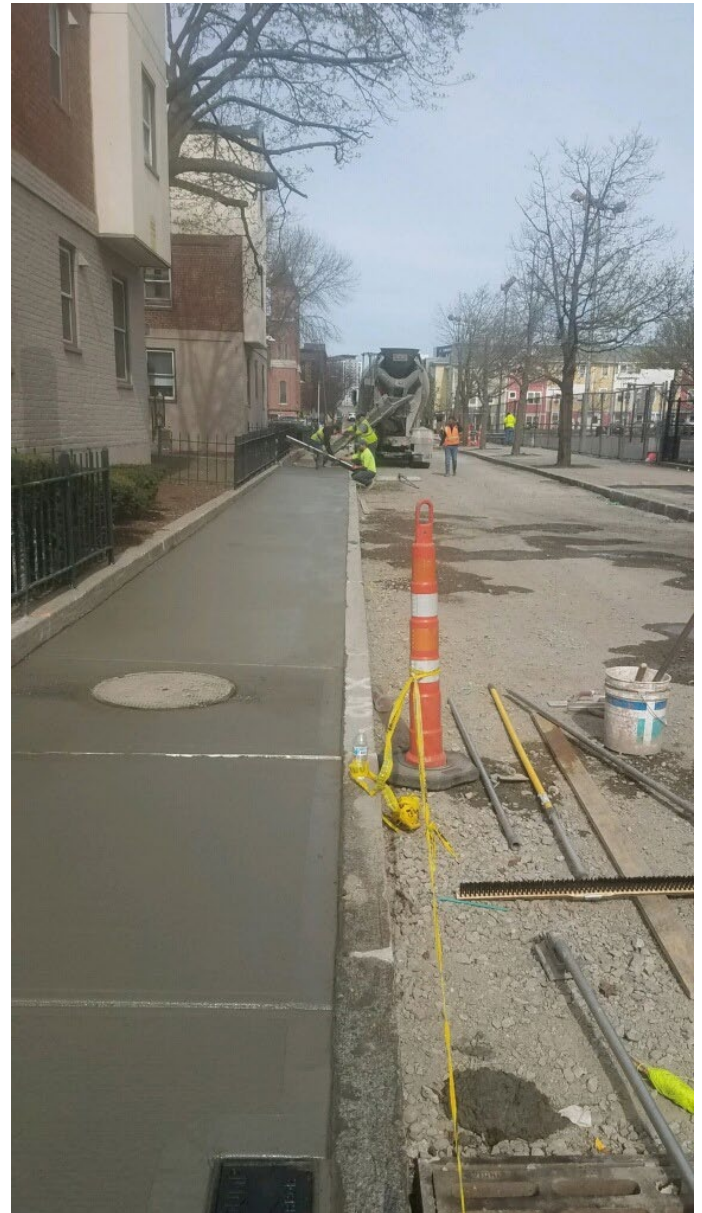

*Concrete sidewalk replacement Flaherty Way*

# INSTALLATION OF NEW STORM DRAINS, SANITARY SEWERS AND WATER MAINS IN SOUTH BOSTON – CONTRACT 1



Contractor: Fed. Corp., Dedham, Massachusetts  
Status as of April 30, 2023

Contract No. 20-309-012

## MAJOR PROGRESS ITEMS – LINEAR FEET (LF) AND % INSTALLED TO DATE

12" – 48" Drain	5,231 LF	93.41%
10" – 24" Sewer	7,764 LF	88.13%
4" – 20" Water Main	5,053 LF	68.23%

## SCHEDULING SUMMARY

Notice to Proceed:	07/06/2021
Work Commenced:	08/10/2021
Anticipated Completion Date:	August 2023

## SCHEDULE ASSESSMENT

The contractor has completed 389 of 400 working days with 97.25% of time used and 2.75% of time remaining.

## PUBLIC AFFAIRS: COMPLAINTS RECEIVED VIA EMAIL AND PHONE (PROJECT TOTAL)


Parking/access	3
Loss/discoloration of water, or low pressure	3
Sewer break/back up	0
Noise/dust/debris	0
Damage	2
Other	7
<b>Project Total</b>	<b>15</b>

## PUBLIC AFFAIRS: CALLS REGARDING OTHER UTILITIES' WORK OR FACILITIES' ACTIVITIES

Parking/access and other issues	0
<b>Other Total</b>	<b>0</b>

## SAFETY

Incidents reported this period	0
<b>Incidents reported to-date</b>	<b>0</b>

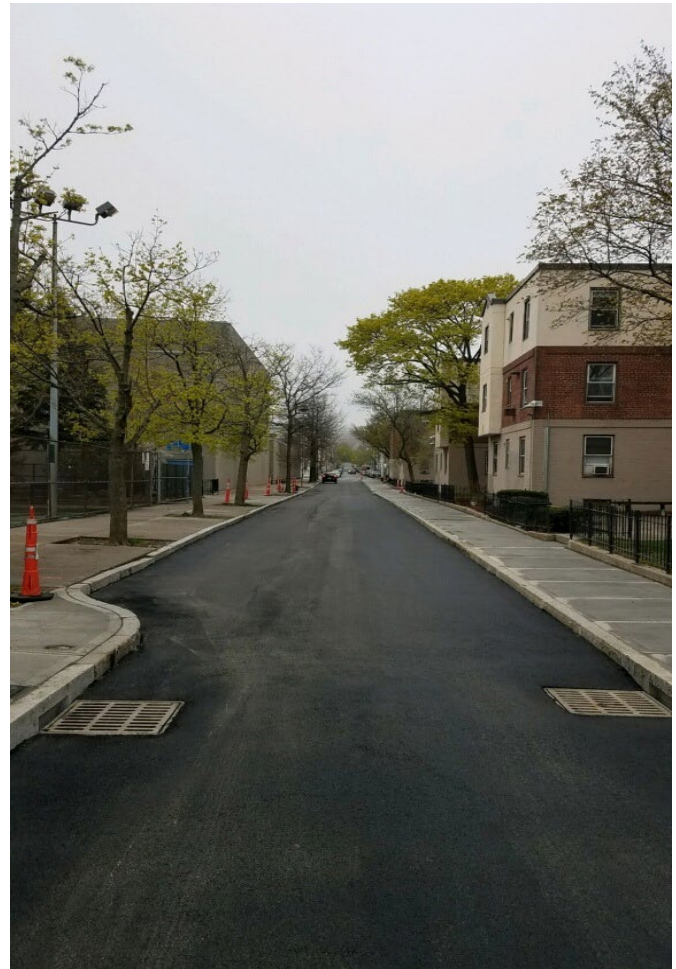

*Temporary paving Flaherty Way*
