



BOSTON WATER & SEWER COMMISSION SOUTH BOSTON SEWER SEPARATION PROJECT

Contract No. 21-309-012

CWSRF NO. 7012

Report for September 11 through September 30, 2023



OVERALL PROJECT UPDATE

The Boston Water and Sewer Commission's (the Commission) South Boston Sewer Separation Project involves separating the combined sewer system in South Boston. The purpose of this project is to reduce pollution levels in Boston Harbor by substantially decreasing the number and volume of Combined Sewer Overflows (CSOs) into Fort Point Channel and Boston Harbor. The separation project is being undertaken by the Commission in association with the Massachusetts Water Resources Authority (MWRA).


The South Boston Sewer Separation Project encompasses an area roughly delineated by Interstate 93 to the west, West Broadway, and West Second Street to the north and east, G Street to the east, and Devine Way to the south. Land use in the project area is characterized by residential neighborhoods; light industrial and large commercial buildings and complexes; small business and retail districts; civic, cultural, and educational facilities; and transportation-related sites.

CONTRACT 2 UPDATE – THROUGH SEPTEMBER 30, 2023

Over the month of September, the project contractor mobilized to the contract site and commenced installation of water by-pass piping along C Street into Old Colony Road, and continuing in Old Colony Road towards Dorchester Avenue. The contractor proceeded to flush, pressure test, and chlorinate by-pass water main in preparation of connecting water services and beginning installation of new water main on C Street.

ONGOING AND UPCOMING WORK

The contractor will commence water main replacement on C Street toward Old Colony Road and continue water main replacement on Old Colony Road towards Dorchester Avenue.

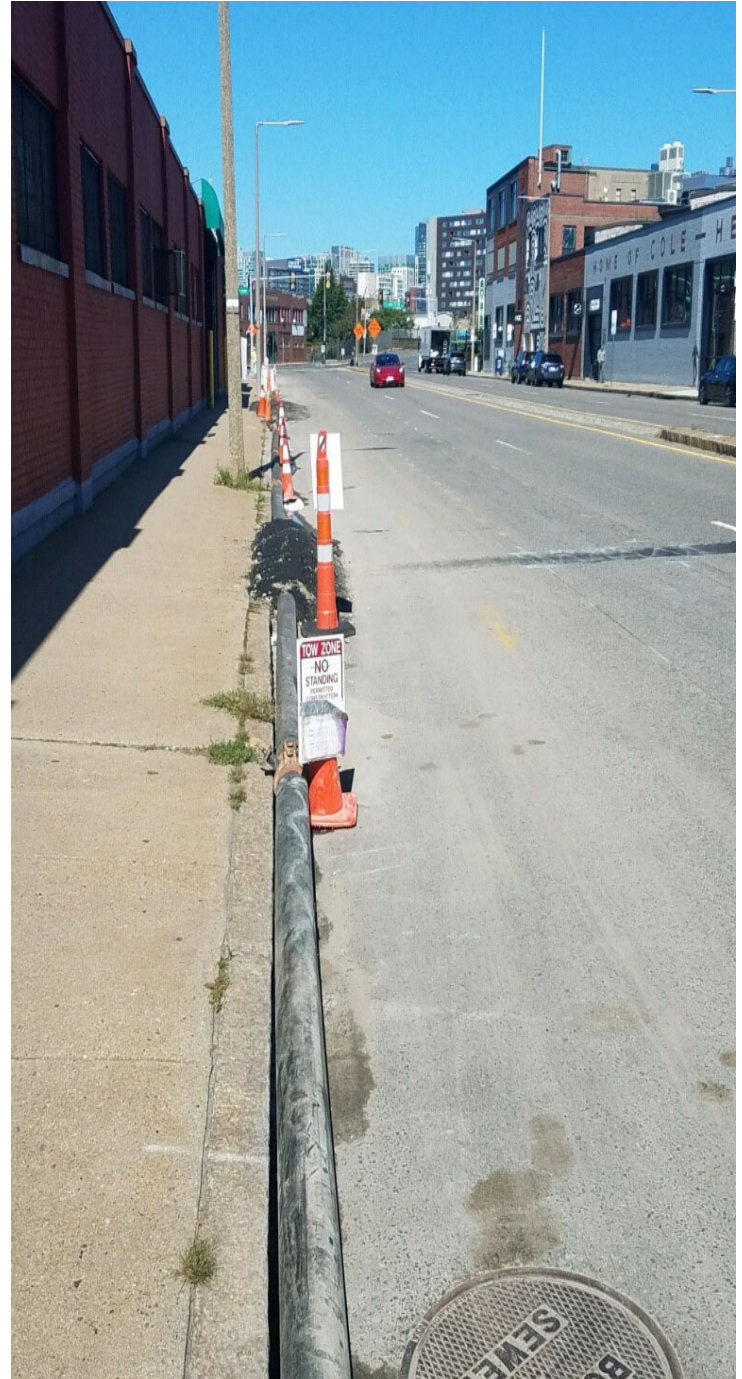

Temporary Water Bypass C Street to Old Colony Road

Contact us at:

Project Field Office Voicemail: 617-865-9299 (daytime) or 617-989-7900 (24/7 emergency)

Email: sbss@bwsc.org



INSTALLATION OF NEW STORM DRAINS, SANITARY SEWERS, AND WATER MAINS IN SOUTH BOSTON – CONTRACT 2



Contractor: Fed. Corp., Dedham, Massachusetts
Status as of September 30, 2023

Contract No. 21-309-012
CWSRF NO.7012

MAJOR PROGRESS ITEMS – LINEAR FEET (LF) AND % INSTALLED TO DATE

12" – 48" Drain	6225 LF	0.00%
10" – 24" Sewer	6920 LF	0.00%
4" – 20" Water Main	11645 LF	0.00%

SCHEDULING SUMMARY

Notice to Proceed: 09/11/2023
Work Commenced: 09/12/2023
Anticipated Completion Date: 04/06/2026

SCHEDULE ASSESSMENT

The contractor has completed five of the contracted 400 working days and 98.75% of time remaining.

PUBLIC AFFAIRS: COMPLAINTS RECEIVED VIA EMAIL AND PHONE (PROJECT TOTAL)

Parking/access	0
Loss/discoloration of water, or low pressure	0
Sewer break/back up	0
Noise/dust/debris	0
Damage	0
Other	0
Project Total	0

PUBLIC AFFAIRS: CALLS REGARDING OTHER UTILITIES' WORK OR FACILITIES' ACTIVITIES

Parking/access and other issues	0
Other Total	0

SAFETY

Incidents reported this period	0
Incidents reported to-date	0

Contact us at:

Project Field Office Voicemail: 617-865-9299 (daytime) or 617-989-7900 (24/7 emergency)

Email: sbss@bwsc.org
