

OVERALL PROJECT UPDATE

The Boston Water and Sewer Commission's (the Commission) South Boston Sewer Separation Project involves separating the combined sewer system in South Boston. The purpose of this project is to reduce pollution levels in Boston Harbor by substantially decreasing the number and volume of Combined Sewer Overflows (CSOs) into Fort Point Channel and Boston Harbor. The separation project is being undertaken by the Commission in association with the Massachusetts Water Resources Authority (MWRA).

The South Boston Sewer Separation Project encompasses an area roughly delineated by Interstate 93 to the west, West Broadway, and West Second Street to the north and east, G Street to the east, and Devine Way to the south. Land use in the project area is characterized by residential neighborhoods; light industrial and large commercial buildings and complexes; small business and retail districts; civic, cultural, and educational facilities; and transportationrelated sites.

CONTRACT 2 UPDATE THROUGH MARCH 31, 2024

Over the month of March, the contractor completed water, sewer, and drain installation on Damrell Street from Dorchester Avenue to Old Colony Avenue. They also completed sewer installation on D Street from Dorchester Avenue into Old Colony Avenue and storm drain on C Street.

ONGOING AND UPCOMING WORK

The contractor will continue sewer installation work on D Street from Old Colony Avenue towards West Seventh Street. Additionally, a second crew will remobilize to Baxter Street and install water main from C Street towards E Street, and continue water main installation on Middle Street from Dorchester Avenue towards Dorchester Street and storm drain and watermain in Woodward Street from Dorchester Avenue to Glover Court.



Sample condition of existing wood pile from D Street.



Temporary paved sewer trench on D Street from Dot Ave towards Old Colony Street.

INSTALLATION OF NEW STORM DRAINS, SANITARY SEWERS, AND WATER MAINS IN SOUTH BOSTON – CONTRACT 2



Contractor: Fed. Corp., Dedham, Massachusetts Status as of March 31, 2024

Contract No. 21-309-012 CWSRF NO.7012

MAJOR PROGRESS ITEMS – LINEAR FEET (LF) AND % INSTALLED TO DATE

12" – 48" Drain	1539 LF	24.72%
10" – 24" Sewer	1984 LF	28.67%
4" – 20" Water Main	4455 LF	38.26%

SCHEDULING SUMMARY

Notice to Proceed:	09/11/2023
Work Commenced:	09/12/2023
Anticipated Completion Date:	04/06/2026

SCHEDULE ASSESSMENT


The contractor has completed ninety-one of the contracted 400 working days with 77.50% of time remaining.

PUBLIC AFFAIRS: COMPLAINTS RECEIVED VIA EMAIL AND PHONE (PROJECT TOTAL)

Project Total	8
Other	4
Damage	1
Noise/dust/debris	0
Sewer break/back up	0
Loss/discoloration of water, or low pressure	1
Parking/access	2

PUBLIC AFFAIRS: CALLS REGARDING OTHER UTILITIES' WORK OR FACILITIES'

ACTIVITIES	
Parking/access and other issues	0
Other Total	0
SAFETY	
Incidents reported this period	0
Incidents reported to-date	0

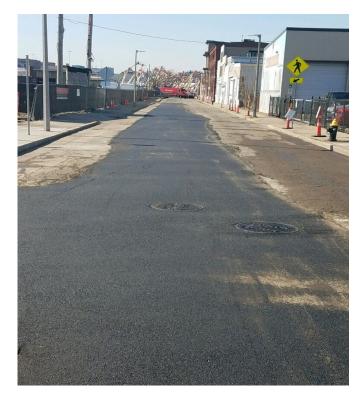

Temporary sewer and drain trench pavement on Damrell Street
