



BOSTON WATER AND SEWER COMMISSION

Fairfield Street

Sewer Improvements

BWSC Contract 17-309-013: November Project Update

Scope of Work: Work under this contract includes the structural lining of the 70"x72" combined sewer and manholes in Fairfield Street. The liner will address groundwater infiltration in the sewer and manholes.

Limits of Work:

- **Fairfield Street:** Beacon Street to Public Alley 427

Completed to Date:


- Installation of sewer by-pass pumps and piping
- Excavation of access hole for pump suction line
- Excavation of access pit for liner inversions
- Excavation of Building sewer services for by-pass pumping
- Pre-cleaning and television inspection

Upcoming Work:

- Installation of structural liner commencing 11/6/17
- Manhole rehabilitations
- The liner installations are a continuous process and will need to take place over two 36-hour periods.



Liner Inversion

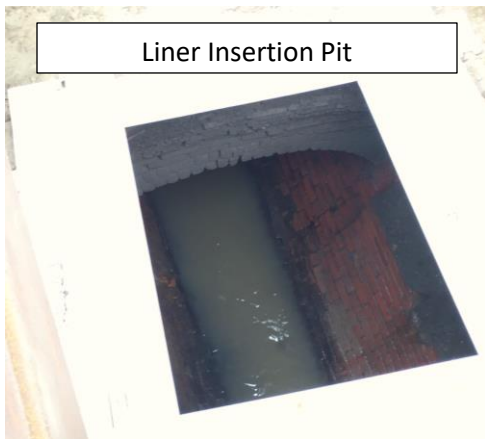

We appreciate your cooperation and understanding as we complete the improvements to the sewer as well as the groundwater table.

PLEASE NOTE:

The structural liner has been fabricated. Insituform will begin mobilizing equipment and crew to Fairfield Street on Monday, November 6 and the liners will be installed this same week, weather dependent. A notice will be distributed to all Fairfield Street abutters 24 hours before the liner is to be installed. Please remember that access to Public Alley 417 will only be available from Exeter Street during the liner installation.

Construction Contacts and additional information:

Commission:

Director of Construction: Irene McSweeney (617) 989-7447
 Project Engineer: Peter Salvatore (617) 989-7363

Contractor: Umbro & Sons Construction

Project Manager: Paul Umbro (857) 492-7260

Emergency: BWSC Headquarters: (617) 989-7000
