

**July UPDATE**


Contractor: Umbro & Sons Construction  
Contract No. 17-308-004

**Work completed in June 2018:**

Cross Street: Completed 12" Water Main  
Completed 16" Water Main

**Upcoming Work in July 2018:**

Blackstone St: Begin bypass Installation

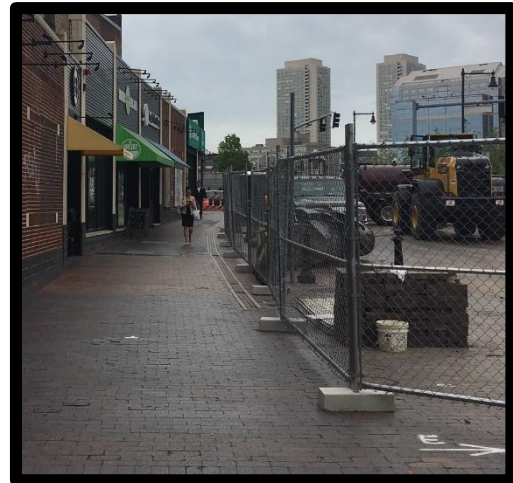

**Fenced in Work Zone - Typical Cross Street**



**Utility Conflicts During Water Main Installation Cross Street**

**Construction Contacts**

**For Additional Information contact:**

**Commission:**

Director of Construction:	Irene McSweeney	617-989-7447
Project Engineer:	Chris Dzidek	617-989-7453
Inspector:	Mike Sferrazza	617-828-5148

**Contractor: Umbro & Sons Construction**

Project Manager	Joseph Umbro Sr.	617-427-0030
-----------------	------------------	--------------

<b><u>24/7 Emergency:</u></b>	BWSC	617-989-7000
-------------------------------	------	--------------

We appreciate your patience and cooperation as we complete this difficult work.

**Permanent paving generally occurs 3-6 months after completion of infrastructure work. Sidewalk restoration is being coordinated with MassDOT ramp project.**

For additional information about this project and other BWSC programs, please visit [www.bwsc.org](http://www.bwsc.org), or follow us on Twitter, Facebook, and Nextdoor.

**THE FOLLOWING PROVIDES AN UPDATE OF COMPLETED WORK AND WORK REMAINING:**

**Water, Drain, Sewer Installation**

<u>Ongoing Work</u>	<u>Scope</u>	<u>Completed</u>	<u>Total</u>	<u>Percent Complete</u>
Blackstone Street	12" & 16" WM	0	950 LF	0%

<u>Completed Work</u>	<u>Scope</u>	<u>Limits</u>	<u>Date Completed</u>
Cross Street	12" & 16" WM	Hanover Street to Endicott Street	6/27/18

<u>Remaining Contract Work</u>	<u>Scope</u>	<u>Limits</u>	<u>Expected Completion</u>
Endicott Street	12" WM 15" SS	Morton Street to Coper Street	Nov 18

SD = Storm Drain  
SS = Sanitary Sewer  
WM = Water Main

Schedule subject to change
