



BOSTON WATER AND SEWER COMMISSION

Tremont Street

Combined Sewer Replacement Project

MAY UPDATE

Scope of Work:

Replacement of 350' of combined sewer on Tremont Street from Stuart Street to Boylston Street under the eastern sidewalk.

- Replacement of 350' feet of existing 12" vitrified clay, concrete encased sewer pipe with new 12" ductile iron pipe
- Replacement of 3 sewer manholes
- Replacement of 2 storm drain catch basins

Project Phasing:

- Phase I: at Stuart Street Intersection
- Phase II: Stuart Street to La Grange Place
- Phase III: La Grange Place to Boylston Street

Status:

Postponed
On-Going
Upcoming

On-Going Work:

- Phase II: Stuart Street to La Grange Place
 - 132' of 12" ductile iron sewer pipe installed
 - 55' of 12" ductile iron sewer pipe remaining
 - One storm drain catch basin installed


Note: Progress of sewer replacement significantly impacted by difficulty in locating existing sewer due to an unknown electric duct bank directly above proposed sewer alignment and unforeseen encounter of granite block foundations that extend further out towards the roadway than shown on record drawings. These conditions have impacted the construction schedule.



Phase II Trench w/ Electric Duct Constraint

CONTRACTOR: RJV Construction

BWSC CONTRACT NO. 16-309-002

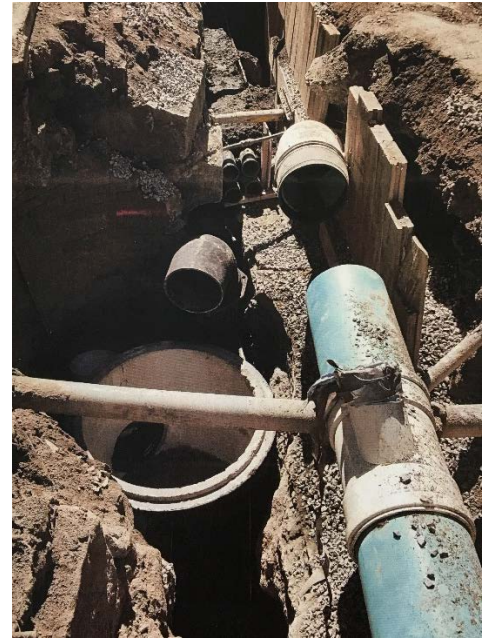

Phase II Temporary Drain Installation

Schedule:

Start Date: November 2017

Projected Completion Date: Summer 2018

Construction on-going, as weather permits.

Amended work hours as of December 2017:

Monday – Friday, 7am to 3pm

Contact Information:

BWSC Representatives

Onsite Inspector: Greg Choukas

Project Engineer: Robert da Silva (617) 989-7457

Director of Construction: Irene McSweeney (617) 989-7447

BWSC Communications: Janet Taylor (617) 989-7354

RJV Construction

Victor Pacella: (617) 504-0315

Office: (781) 821-1469

24/7 Emergency

BWSC: (617) 989-7000
