



SOUTH BOSTON SEWER SEPARATION

Report for November 1 through November 30, 2021

OVERALL PROJECT UPDATE

The Boston Water and Sewer Commission's (the Commission) South Boston Sewer Separation Project involves separating the combined sewer system in South Boston. The purpose of this federal court ordered project is to reduce pollution levels in Boston Harbor by substantially decreasing the number and volume of Combined Sewer Overflows (CSOs) into Fort Point Channel and Boston Harbor. The separation project is being undertaken by the Commission on behalf of the Massachusetts Water Resources Authority (MWRA).

The South Boston Sewer Separation Project encompasses an area roughly delineated by Interstate 93 to the west, West Broadway and West Second Street to the north and east, G Street to the east, and Devine Way to the south. Land use in the project area is characterized by residential neighborhoods; light industrial and large commercial buildings and complexes; small business and retail districts; civic, cultural, and educational facilities; and transportation related sites.

CONTRACT 1 UPDATE – THROUGH NOVEMBER 30, 2021

Contract 1 is ongoing with storm drain, sanitary sewer and manhole installation on various streets. Work on A Street has been substantially completed this period.


Work on A Street included the installation of approximately 250 linear feet of 10-inch sewer and 278 linear feet of 12-inch storm drain.

ONGOING AND UPCOMING WORK

Work on Silver Street will be performed in two sections, from A Street to the South Boston Bypass Road and from Dorchester Avenue to A Street. Work will commence in the beginning of December and continue over the next three weeks, weather permitting.



Temporary pavement on A Street.

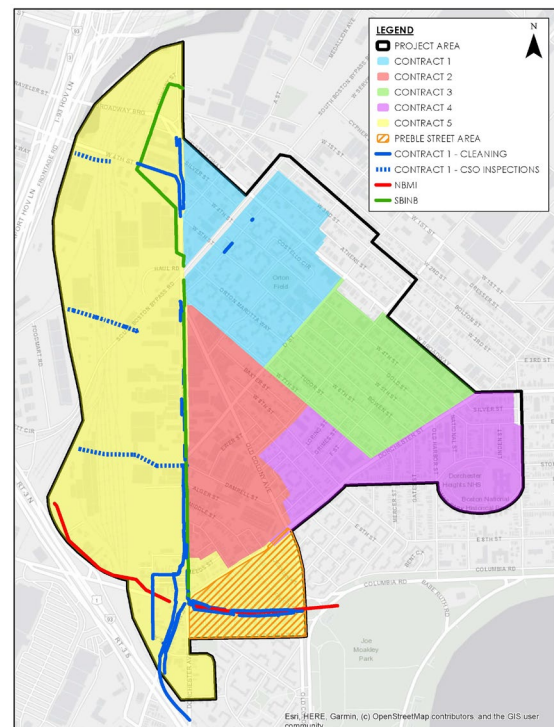

Project map, noting different contract work areas.

INSTALLATION OF NEW STORM DRAINS, SANITARY SEWERS AND WATER MAINS IN SOUTH BOSTON – CONTRACT 1



Contractor: Fed. Corp., Dedham, Massachusetts
Status as of November 30, 2021

Contract No. 20-309-012

MAJOR PROGRESS ITEMS – LINEAR FEET (LF) AND % INSTALLED TO DATE

12" – 48" Drain	1,533 LF	27.4%
10" – 24" Sewer	1,576 LF	17.9%
4" – 20" Water Main	0 LF	0%

SCHEDULING SUMMARY

Notice to Proceed:	07/06/2021
Work Commenced:	08/10/2021
Completion Date:	02/13/2023

SCHEDULE ASSESSMENT

The contractor has completed 74 of 400 working days with 18.5% of time used and 81.5% of time remaining.

PUBLIC AFFAIRS: COMPLAINTS RECEIVED VIA EMAIL AND PHONE (PROJECT TOTAL)

Parking/access	0
Loss/discoloration of water, or low pressure	0
Sewer break/back up	0
Noise/dust/debris	0
Damage	0
Other	2
Project Total	2

PUBLIC AFFAIRS: CALLS REGARDING OTHER UTILITIES' WORK OR FACILITIES' ACTIVITIES

Parking/access and other issues	0
Other Total	0

SAFETY

Incidents reported this period	0
Incidents reported to- date	0



*New drain manhole installed at A Street near
Broadway.*
