



SOUTH BOSTON SEWER SEPARATION

Report for February 1 through February 28, 2022

OVERALL PROJECT UPDATE

The Boston Water and Sewer Commission's (the Commission) South Boston Sewer Separation Project involves separating the combined sewer system in South Boston. The purpose of this project is to reduce pollution levels in Boston Harbor by substantially decreasing the number and volume of Combined Sewer Overflows (CSOs) into Fort Point Channel and Boston Harbor. The separation project is being undertaken by the Commission in association with the Massachusetts Water Resources Authority (MWRA).

The South Boston Sewer Separation Project encompasses an area roughly delineated by Interstate 93 to the west, West Broadway, and West Second Street to the north and east, G Street to the east, and Devine Way to the south. Land use in the project area is characterized by residential neighborhoods; light industrial and large commercial buildings and complexes; small business and retail districts; civic, cultural, and educational facilities; and transportation related sites.


CONTRACT 1 UPDATE – THROUGH FEBRUARY 28, 2022

Contract 1 construction remained on hold throughout February to continue to observe the winter moratorium as required by contract.

Contractor was permitted to commence non excavation work which included seven days of cleaning existing combined sewer line on B Street, from West Seventh Street to Athens Street.

ONGOING AND UPCOMING WORK

Next scheduled areas during the winter months include continued combined sewer cleaning and CCTV on B Street, drainage work at Dorchester Avenue into Silver Street, and downstream sewer manhole on B Street. This work is dependent on weather conditions and the waiving of the winter construction moratorium.

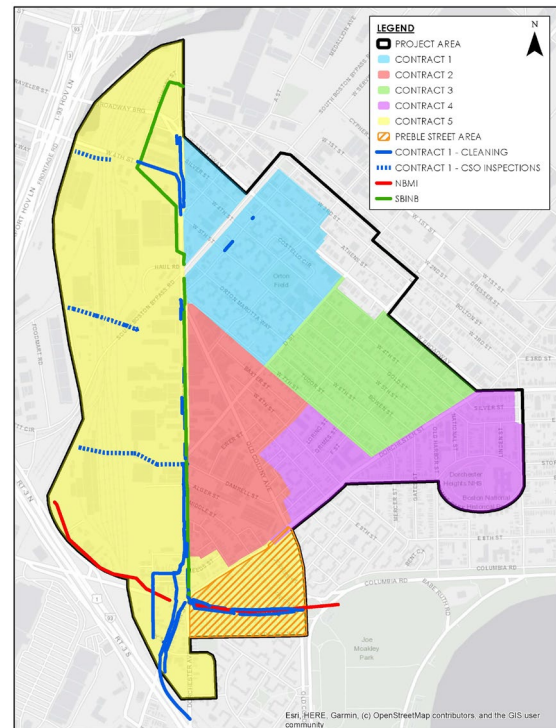

Project map, noting different contract work areas.

INSTALLATION OF NEW STORM DRAINS, SANITARY SEWERS AND WATER MAINS IN SOUTH BOSTON – CONTRACT 1



Contractor: Fed. Corp., Dedham, Massachusetts
Status as of February 28, 2022

Contract No. 20-309-012

MAJOR PROGRESS ITEMS – LINEAR FEET (LF) AND % INSTALLED TO DATE

12" – 48" Drain	1,833 LF	32.73%
10" – 24" Sewer	2,030 LF	23.04%
4" – 20" Water Main	0 LF	0%

SCHEDULING SUMMARY

Notice to Proceed: 07/06/2021
Work Commenced: 08/10/2021
Completion Date: 02/13/2023

SCHEDULE ASSESSMENT

The contractor has completed 99 of 400 working days with 24.75% of time used and 75.25% of time remaining.

PUBLIC AFFAIRS: COMPLAINTS RECEIVED VIA EMAIL AND PHONE (PROJECT TOTAL)

Parking/access	0
Loss/discoloration of water, or low pressure	0
Sewer break/back up	0
Noise/dust/debris	0
Damage	0
Other	2
Project Total	2

PUBLIC AFFAIRS: CALLS REGARDING OTHER UTILITIES' WORK OR FACILITIES' ACTIVITIES

Parking/access and other issues	0
Other Total	0

SAFETY

Incidents reported this period	0
Incidents reported to- date	0



Set up for Combined Sewer Cleaning on B Street



Pipe Cleaning B Street
