



SOUTH BOSTON SEWER SEPARATION

Report for September 1 through September 30, 2022

OVERALL PROJECT UPDATE

The Boston Water and Sewer Commission's (the Commission) South Boston Sewer Separation Project involves separating the combined sewer system in South Boston. The purpose of this project is to reduce pollution levels in Boston Harbor by substantially decreasing the number and volume of Combined Sewer Overflows (CSOs) into Fort Point Channel and Boston Harbor. The separation project is being undertaken by the Commission in association with the Massachusetts Water Resources Authority (MWRA).


The South Boston Sewer Separation Project encompasses an area roughly delineated by Interstate 93 to the west, West Broadway, and West Second Street to the north and east, G Street to the east, and Devine Way to the south. Land use in the project area is characterized by residential neighborhoods; light industrial and large commercial buildings and complexes; small business and retail districts; civic, cultural, and educational facilities; and transportation-related sites.

CONTRACT 1 UPDATE – THROUGH SEPTEMBER 30, 2022

Over the month of September, the contractor completed drain installation on C Street and West Third Street; watermain replacement on West Broadway, C Street, and B Street; and placed temporary pavement and line striping on West Broadway, B Street, and C Street.

ONGOING AND UPCOMING WORK

Currently, the contractor is installing water main on West Third Street from B Street to C Street. Upcoming sewer, water and drain replacement work is anticipated to take place on Athens Street and West Seventh Street.

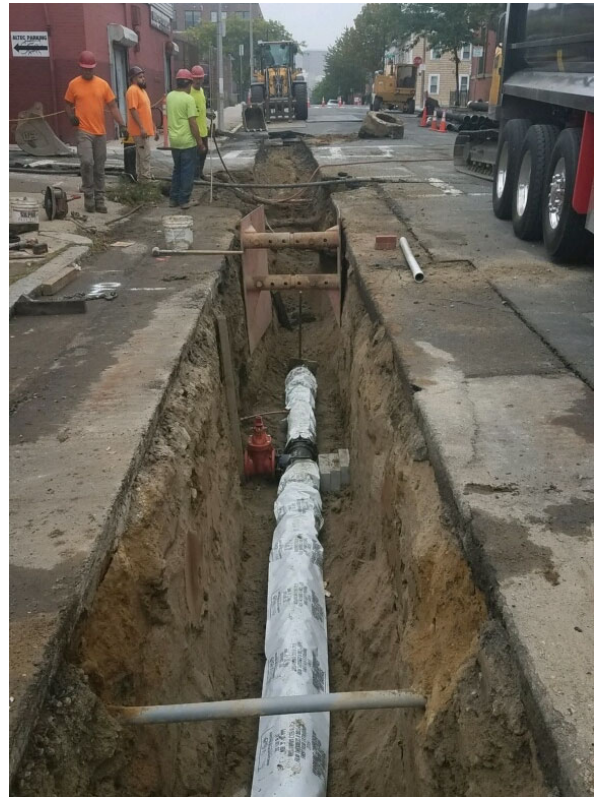

Water Main Replacement on B Street



Temporary Paving on B Street at Crowley Rogers Way

INSTALLATION OF NEW STORM DRAINS, SANITARY SEWERS AND WATER MAINS IN SOUTH BOSTON – CONTRACT 1



Contractor: Fed. Corp., Dedham, Massachusetts
Status as of September 30, 2022

Contract No. 20-309-012

MAJOR PROGRESS ITEMS – LINEAR FEET (LF) AND % INSTALLED TO DATE

12" – 48" Drain	3,344 LF	59.71%
10" – 24" Sewer	4,415 LF	50.11%
4" – 20" Water Main	2,225 LF	30.05%

SCHEDULING SUMMARY

Notice to Proceed:	07/06/2021
Work Commenced:	08/10/2021
Completion Date:	02/13/2023

SCHEDULE ASSESSMENT

The contractor has completed 243 of 400 working days with 60.75% of time used and 39.25% of time remaining.

PUBLIC AFFAIRS: COMPLAINTS RECEIVED VIA EMAIL AND PHONE (PROJECT TOTAL)

Parking/access	2
Loss/dicoloration of water, or low pressure	2
Sewer break/back up	0
Noise/dust/debris	0
Damage	1
Other	4
Project Total	9

PUBLIC AFFAIRS: CALLS REGARDING OTHER UTILITIES' WORK OR FACILITIES' ACTIVITIES

Parking/access and other issues	0
Other Total	0

SAFETY

Incidents reported this period	0
Incidents reported to-date	0



Pile Removal at Special Manhole A on West Seventh Street
