



SOUTH BOSTON SEWER SEPARATION

Report for October 1 through October 31, 2022

OVERALL PROJECT UPDATE

The Boston Water and Sewer Commission's (the Commission) South Boston Sewer Separation Project involves separating the combined sewer system in South Boston. The purpose of this project is to reduce pollution levels in Boston Harbor by substantially decreasing the number and volume of Combined Sewer Overflows (CSOs) into Fort Point Channel and Boston Harbor. The separation project is being undertaken by the Commission in association with the Massachusetts Water Resources Authority (MWRA).


The South Boston Sewer Separation Project encompasses an area roughly delineated by Interstate 93 to the west, West Broadway, and West Second Street to the north and east, G Street to the east, and Devine Way to the south. Land use in the project area is characterized by residential neighborhoods; light industrial and large commercial buildings and complexes; small business and retail districts; civic, cultural, and educational facilities; and transportation-related sites.

CONTRACT 1 UPDATE – THROUGH OCTOBER 31, 2022

Over the month of October, the project contractor completed drain connections on B Street; completed watermain installation on West Third Street; commenced sewer and watermain installation on Athens Street and West Seventh Street.

ONGOING AND UPCOMING WORK

Currently, the contractor is completing watermain installation on Athens Street from B Street towards C Street, sewer main installation from Haul Road to B Street and sewer, water and drain replacement work on West Seventh Street from B Street towards C Street.

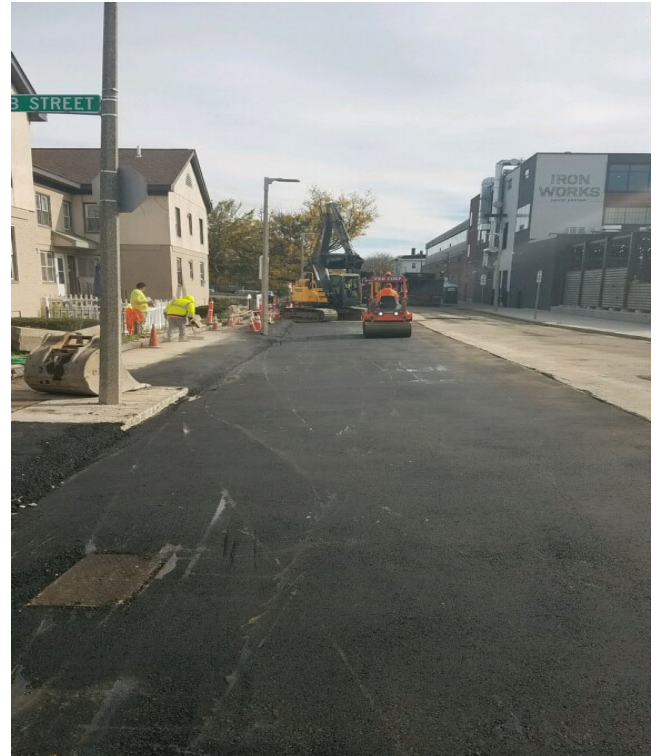

Temporary Paving West Seventh St



12-inch Watermain Installation at B Street and West Seventh Street

INSTALLATION OF NEW STORM DRAINS, SANITARY SEWERS AND WATER MAINS IN SOUTH BOSTON – CONTRACT 1



Contractor: Fed. Corp., Dedham, Massachusetts
Status as of October 31, 2022

Contract No. 20-309-012

MAJOR PROGRESS ITEMS – LINEAR FEET (LF) AND % INSTALLED TO DATE

12" – 48" Drain	3,371 LF	60.20%
10" – 24" Sewer	4,468 LF	50.72%
4" – 20" Water Main	2,937 LF	39.66%

SCHEDULING SUMMARY

Notice to Proceed:	07/06/2021
Work Commenced:	08/10/2021
Completion Date:	02/13/2023

SCHEDULE ASSESSMENT

The contractor has completed 263 of 400 working days with 65.75% of time used and 34.25% of time remaining.

PUBLIC AFFAIRS: COMPLAINTS RECEIVED VIA EMAIL AND PHONE (PROJECT TOTAL)

Parking/access	2
Loss/discoloration of water, or low pressure	2
Sewer break/back up	0
Noise/dust/debris	0
Damage	1
Other	5
Project Total	10

PUBLIC AFFAIRS: CALLS REGARDING OTHER UTILITIES' WORK OR FACILITIES' ACTIVITIES

Parking/access and other issues	0
Other Total	0

SAFETY

Incidents reported this period	0
Incidents reported to-date	0



8-inch Watermain Installation Athens Street
