



SOUTH BOSTON SEWER SEPARATION

Report for November 1 through November 30, 2022

OVERALL PROJECT UPDATE

The Boston Water and Sewer Commission's (the Commission) South Boston Sewer Separation Project involves separating the combined sewer system in South Boston. The purpose of this project is to reduce pollution levels in Boston Harbor by substantially decreasing the number and volume of Combined Sewer Overflows (CSOs) into Fort Point Channel and Boston Harbor. The separation project is being undertaken by the Commission in association with the Massachusetts Water Resources Authority (MWRA).


The South Boston Sewer Separation Project encompasses an area roughly delineated by Interstate 93 to the west, West Broadway, and West Second Street to the north and east, G Street to the east, and Devine Way to the south. Land use in the project area is characterized by residential neighborhoods; light industrial and large commercial buildings and complexes; small business and retail districts; civic, cultural, and educational facilities; and transportation-related sites.

CONTRACT 1 UPDATE – THROUGH NOVEMBER 30, 2022

Over the month of November, the contractor completed drain, sewer, and water installation on Athens Street; water and sewer installation on West Seventh Street from B Street to C Street; and commenced watermain installation on Flaherty Way.

ONGOING AND UPCOMING WORK

Currently, the contractor is working on water main installation on Flaherty Way from B Street towards D Street, sewer work on West Fourth Street, and sewer and water main replacement work on Crowley Rogers Way from B Street towards Dalessio Court.

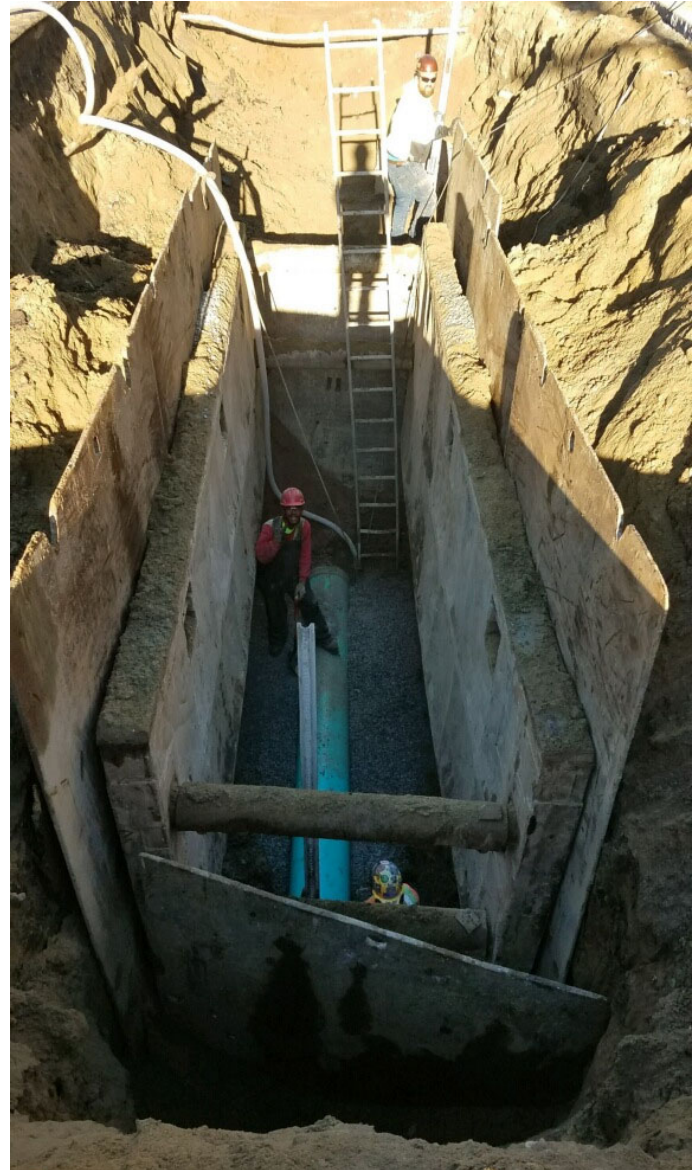

18-inch sewer installation on West Seventh Street

INSTALLATION OF NEW STORM DRAINS, SANITARY SEWERS AND WATER MAINS IN SOUTH BOSTON – CONTRACT 1



Contractor: Fed. Corp., Dedham, Massachusetts
Status as of November 30, 2022

Contract No. 20-309-012

MAJOR PROGRESS ITEMS – LINEAR FEET (LF) AND % INSTALLED TO DATE

12" – 48" Drain	3,751 LF	66.98%
10" – 24" Sewer	5,461 LF	61.99%
4" – 20" Water Main	4,246 LF	57.34%

SCHEDULING SUMMARY

Notice to Proceed: 07/06/2021
Work Commenced: 08/10/2021
Completion Date: 02/13/2023

SCHEDULE ASSESSMENT

The contractor has completed 283 of 400 working days with 70.75% of time used and 29.25% of time remaining.

PUBLIC AFFAIRS: COMPLAINTS RECEIVED VIA EMAIL AND PHONE (PROJECT TOTAL)

Parking/access	2
Loss/discoloration of water, or low pressure	2
Sewer break/back up	0
Noise/dust/debris	0
Damage	1
Other	6

Project Total 11

PUBLIC AFFAIRS: CALLS REGARDING OTHER UTILITIES' WORK OR FACILITIES' ACTIVITIES

Parking/access and other issues	0
Other Total	0

SAFETY

Incidents reported this period	0
Incidents reported to-date	0



Temporary Paving Athens Street
