




BOSTON WATER & SEWER COMMISSION
EAST BOSTON SEWER SEPARATION PROJECT
Contract No. 21-309-002
CWSRF NO. 16690
Report for March 1 through March 31, 2026



OVERALL PROJECT UPDATE

The Boston Water and Sewer Commission's (the Commission) East Boston Sewer Separation Project involves separating the combined sewer system in East Boston. The purpose of this project is to separate the combined sewer system by installing new sewer and drain pipes. This will improve water quality by reducing the number and volume of Combined Sewer Overflows (CSOs). The separation project is being undertaken by the Commission in association with the Massachusetts Water Resources Authority (MWRA).

The East Boston Sewer Separation Project encompasses an area roughly delineated by White Street and Condor Street to the north; by William F. McClellan Highway (Route 1A) and Bremen Street to the east; by Maverick Street and Sumner Street to the south and by Meridian Street to the west. Land use in the project area is characterized by high-density residential neighborhoods, commercial and light industrial buildings, municipal and recreational areas, and transportation related sites.

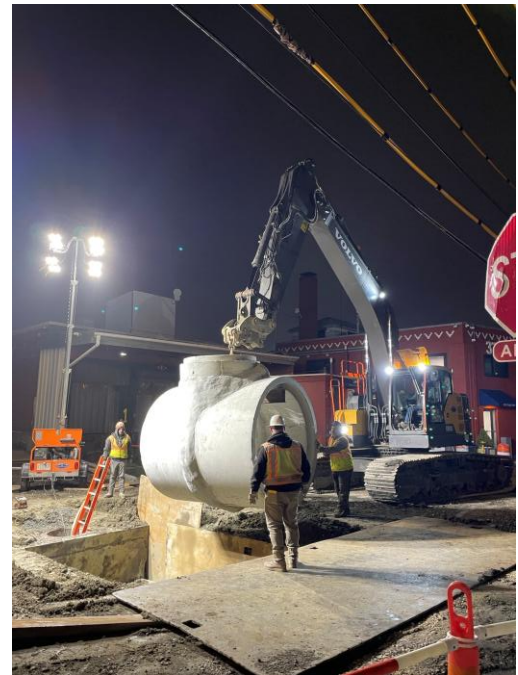


Drain tee manhole installation in Eagle Square

CONTRACT 1 UPDATE THROUGH MARCH 31, 2026

Over the month of March, the contractor installed a new sewer mainline on Princeton Street between Eagle Square and Shelby Street. Additionally, the contractor continued installation of a new sewer mainline and manholes in East Eagle Street.

ONGOING AND UPCOMING WORK

The contractor will install a new storm drain mainline and manholes in Eagle Square between East Eagle Street and Princeton Street. The contractor will also install new sewer and storm drains in Glendon Street and a new sewer main on Falcon Street. The contractor will also begin installation of temporary water bypass on Frankfort Street, Swift Terrace, and Swift Street. In addition to installing new storm drains, the Commission will be replacing or repairing deteriorated sewer pipes and replacing aged water mains.

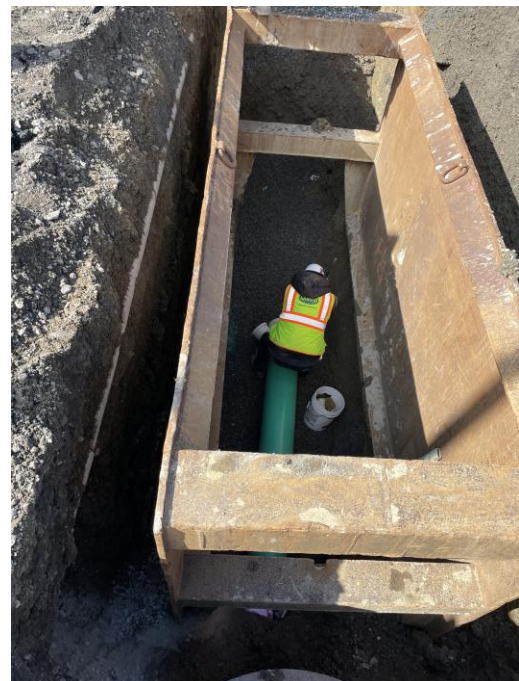

Sewer main installation in Princeton Street



INSTALLATION OF NEW STORM DRAINS, SANITARY SEWERS, AND WATER MAINS IN EAST BOSTON – CONTRACT 1



Contractor: P. Gioioso & Sons, Inc., Hyde Park, Massachusetts
Status as of March 31, 2026

Contract No. 21-309-002
CWSRF NO. 16690

MAJOR PROGRESS ITEMS – LINEAR FEET (LF) AND % INSTALLED TO DATE

12" – 72" Drain	5 LF	0.07%
10" – 24" Sewer	514 LF	17.12%
4" – 30" Water Main	0 LF	0.00%
CIPP Lining	0 LF	0.00%

SCHEDULING SUMMARY

Notice to Proceed: 09/09/2025
Work Commenced: 09/24/2025
Anticipated Completion Date: 09/14/2027

SCHEDULE ASSESSMENT

The contractor has completed 71 of the contracted 500 working days and has 85.8% of time remaining.
