


OVERALL PROJECT UPDATE

The Boston Water and Sewer Commission's (the Commission) East Boston Sewer Separation Project involves separating the combined sewer system by installing new sewer and drain pipes. This will improve water quality in Boston Harbor by reducing the number and volume of Combined Sewer Overflows (CSOs). The separation project is being undertaken by the Commission in association with the Massachusetts Water Resources Authority (MWRA).

The Project encompasses an area roughly delineated by White Street and Condor Street to the north; by William F. McClellan Highway (Route 1A) and Bremen Street to the east; by Maverick Street and Sumner Street to the south; and by Meridian Street to the west. Land use in the project area is characterized by high-density residential neighborhoods, commercial and light industrial buildings, municipal and recreational areas and transportation-related sites.

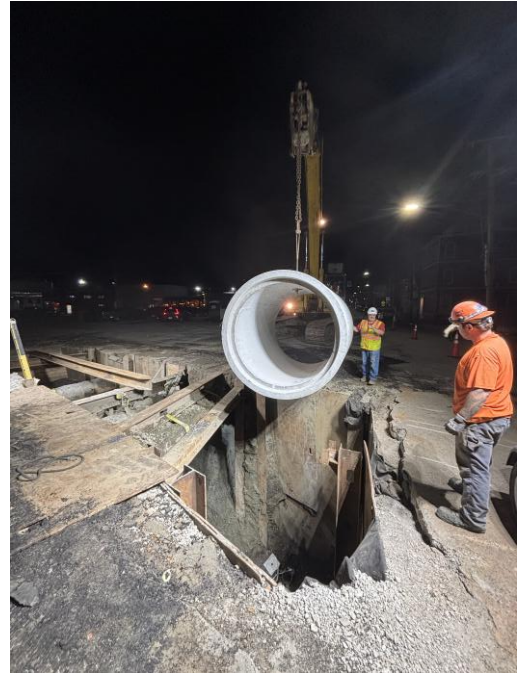

CONTRACT 1 UPDATE THROUGH JULY 31, 2026

During the month of July, the contractor continued installing storm drain mainline in Eagle Square, continues installing water main in East Eagle Street, and continued installing water main and drainage infiltration structures on Swift Terrace and Swift Street. The contractor also began installation of temporary water bypass on Chelsea Street between Eagle Square and Day Square in preparation of sewer and drain installation on Chelsea Street.

ONGOING AND UPCOMING WORK

The contractor will complete installing drain mainline in Eagle Square. The contractor will begin installation of watermain in Chelsea Street, and drain mainline in East Eagle Street. The contractor will also continue preparatory work for sewer and drain installation in Chelsea Street.



Drain installation in Eagle Square



INSTALLATION OF NEW STORM DRAINS, SANITARY SEWERS, AND WATER MAINS IN SOUTH BOSTON – CONTRACT 3



Contractor: P. Gioioso & Sons, Inc., Hyde Park, Massachusetts
Status as of July 31, 2026

Contract No. 22-309-012
CWSRF NO.7012

MAJOR PROGRESS ITEMS – LINEAR FEET (LF) AND % INSTALLED TO DATE

4" – 30" Water Main	2610 LF	16.65%
10" – 24" Sewer	1700 LF	56.63%
12" – 48" Drain	810 LF	10.89%
CIPP Lining	2460 LF	31.57%

SCHEDULING SUMMARY

Notice to Proceed: 09/09/2025
Work Commenced: 09/24/2025
Anticipated Completion Date: 09/14/2027

SCHEDULE ASSESSMENT

The contractor has completed 152 of the contracted 500 working days and has 69.6% of time remaining.

Contact us at:

Project Field Office Voicemail: 617-865-9299 (daytime) or 617-989-7900 (24/7 emergency)

Email: eastbostonsewerseparation@bwsc.org
