

August UPDATE

Contractor: D'Allessandro Corp.

Contract NO. 16-308-005

Scope of Work:


Install 2650 LF of 16" Water Main

Work completed in July 2018:

Installed 700 LF of 16" Water Main Between East Canton Street and Wareham Street
(25% Complete)

Upcoming Work in August 2018:

Continue Water Main Installation at Wareham Street
Second Crew to Continue Water Main Installation at East Berkeley Street

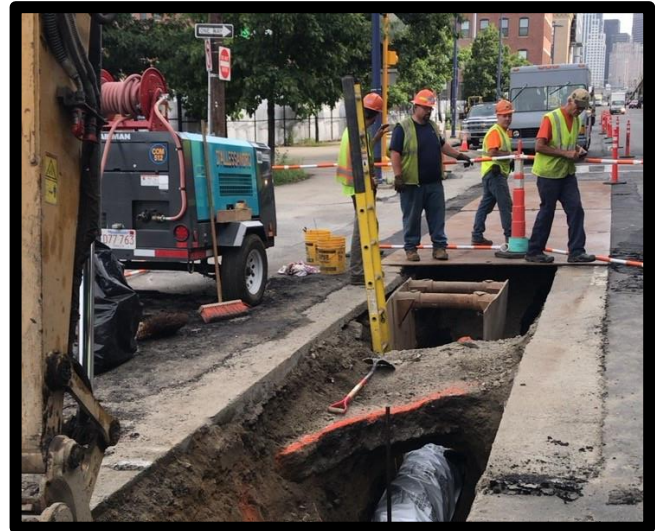

**Water Main Installation
Albany Street**



**Typical Water Main Bypass
Albany Street**

Construction Contacts

For Additional Information Contact:

Commission:

Director of Construction:	Irene McSweeney	617-989-7447
Project Engineer:	Chris Dzidek	617-989-7453
Inspector:	Dan Day	617-719-6612

Contractor: D'Allessandro Corp.

Project Manager	Derek Grossi	508-559-6400
-----------------	--------------	--------------

<u>24/7 Emergency:</u>	BWSC	617-989-7000
-------------------------------	------	--------------

We appreciate your patience and cooperation as we complete this difficult work.

Temporary paving is installed as work progresses.

Permanent paving generally occurs 3-6 months after completion of infrastructure work.

For additional information about this project and other BWSC programs, please visit www.bwsc.org, or follow us on Twitter, Facebook, and Nextdoor.
