



BOSTON WATER AND SEWER COMMISSION

Tremont Street

Combined Sewer Replacement Project

DECEMBER UPDATE

Scope of Work:

Replacement of 350' of combined sewer on Tremont Street from Stuart Street to Boylston Street underneath the eastern sidewalk.

- Replacement of 350' feet of existing 12" vitrified clay, concrete encased sewer pipe with new 12" ductile iron pipe
- Replacement of 3 sewer manholes
- Replacement of 2 storm drain catch basins

Project Phasing:

- Phase I: Tremont Street – at Stuart Street Intersection
- Phase II: Tremont Street – Stuart Street to La Grange Place
- Phase III: Tremont Street – La Grange Place to Boylston Street

On-Going Work:


- Phase I: at Stuart Street intersection
 - Access pit excavation
 - Installation of combined sewer pipe connection into Stuart Street
- Phase II: Stuart Street to La Grange Place
 - Due to complex utilities, transition into Phase II to see if access to sewer at Stuart Street intersection is more viable



Sewer Replacement Excavation

CONTRACTOR: RJV Construction

BWSC CONTRACT NO. 16-309-002

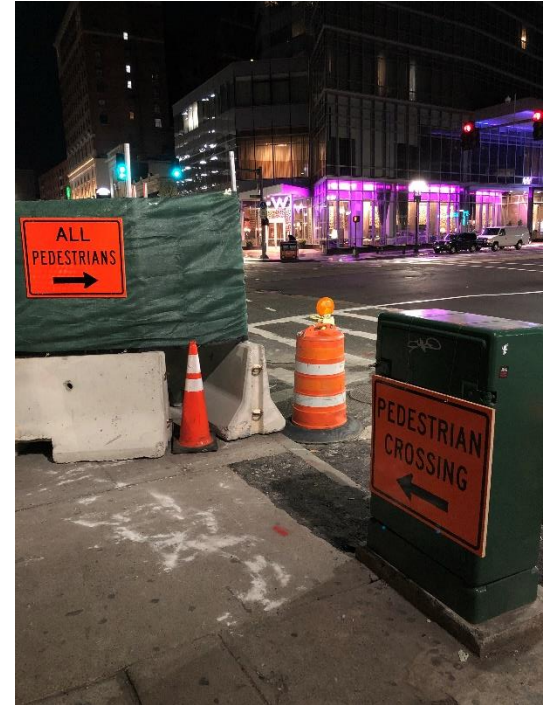

Phase I Work Zone Barrier

Schedule:

Start Date: November 2017

Projected Completion Date: Spring 2018
(Construction anticipated through Winter)

**Amended work hours as of 12/4/17:
Monday – Friday, 7am to 3pm**

Contact Information

BWSC Representatives

Onsite Inspector: Tom Hanlon

Project Engineer: Robert da Silva (617) 989-7457

Director of Construction: Irene McSweeney (617) 989-7447

BWSC Communications: Janet Taylor (617) 989-7354

RJV Construction

Victor Pacella: (617) 504-0315

Office: (781) 821-1469

24/7 Emergency

BWSC: (617) 989-7000
