



BOSTON WATER & SEWER COMMISSION
EAST BOSTON SEWER SEPARATION PROJECT
Contract No. 21-309-002
CWSRF NO. 16690
Report for April 1 through April 30, 2026



OVERALL PROJECT UPDATE

The Boston Water and Sewer Commission's (the Commission) East Boston Sewer Separation Project involves separating the combined sewer system in East Boston. The purpose is to separate the combined sewer system by installing new sewer and drain pipes. This will improve water quality by reducing the number and volume of Combined Sewer Overflows (CSOs). The project is being undertaken by the Commission with the Massachusetts Water Resources Authority (MWRA).

The East Boston Sewer Separation Project encompasses an area roughly delineated by White Street and Condor Street to the north; by William F. McClellan Highway (Route 1A) and Bremen Street to the east; by Maverick Street and Sumner Street to the south and by Meridian Street to the west. Land use in the project area is characterized by high-density residential neighborhoods, commercial and light industrial buildings, municipal and recreational areas and transportation related sites.

CONTRACT 1 UPDATE THROUGH APRIL 30, 2026


In April, the contractor installed a new storm drain mainline and manholes on Glendon Street and Eagle Square, a new sewer mainline and manholes on Frankfort Street, and a new water main in East Eagle Street. The contractor also performed downspout disconnections on Trenton Street, Lexington Street and East Eagle Street.

ONGOING AND UPCOMING WORK

The contractor will continue installation of water, sewer and drain mainlines on East Eagle Street. The contractor will continue installation of sewer mainline and manholes on Frankfort Street as well as new drainage infiltration structures. The Contractor will begin installation of new a water main on Frankfort Street, Swift Street and Swift Terrace. The Contractor will also begin performing cured in place pipe (CIPP) lining on Falcon Street, Condor Street, Glendon Street, Trenton Street, Prescott Street, Lexington Street, Bennington Street, Bremen Street and Saratoga Street.



72" Storm drain installation in Eagle Square

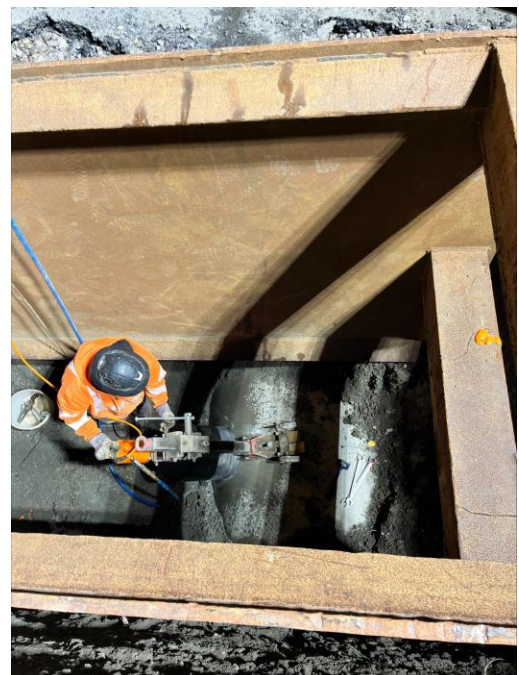

Coring 72" storm drain for catch basin connection in Eagle Square

Contact us at:

Project Field Office Voicemail: 617-372-9158 (daytime) or 617-989-7900 (24/7 emergency)

Email: eastbostonsewerseparationproject@bwsc.org



INSTALLATION OF NEW STORM DRAINS, SANITARY SEWERS, AND WATER MAINS IN EAST BOSTON – CONTRACT 1



Contractor: P. Gioioso & Sons, Inc., Hyde Park, Massachusetts
Status as of April 30, 2026

Contract No. 21-309-002
CWSRF NO. 16690

MAJOR PROGRESS ITEMS – LINEAR FEET (LF) AND % INSTALLED TO DATE

12" – 72" Drain	240 LF	3.21%
10" – 24" Sewer	580 LF	19.43%
4" – 30" Water Main	0 LF	0.00%
CIPP Lining	0 LF	0.00%

SCHEDULING SUMMARY

Notice to Proceed: 09/09/2025
 Work Commenced: 09/24/2025
 Anticipated Completion Date: 09/14/2027

SCHEDULE ASSESSMENT

The contractor has completed 90 of the contracted 500 working days and has 82.0% of time remaining.

Contact us at:

Project Field Office Voicemail: 617-372-9158 (daytime) or 617-989-7900 (24/7 emergency)

Email: eastbostonsewarseparationproject@bwsc.org
